
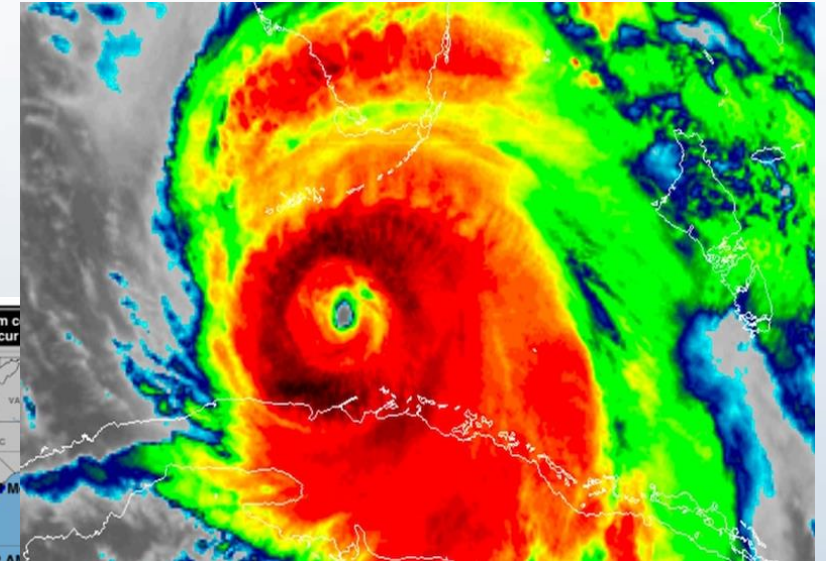


# Hurricane Irma Update

## Presentation Summary

- After Action Review Process
- Current After Actions in Progress
- Planned Objectives 2018 Hurricane Season

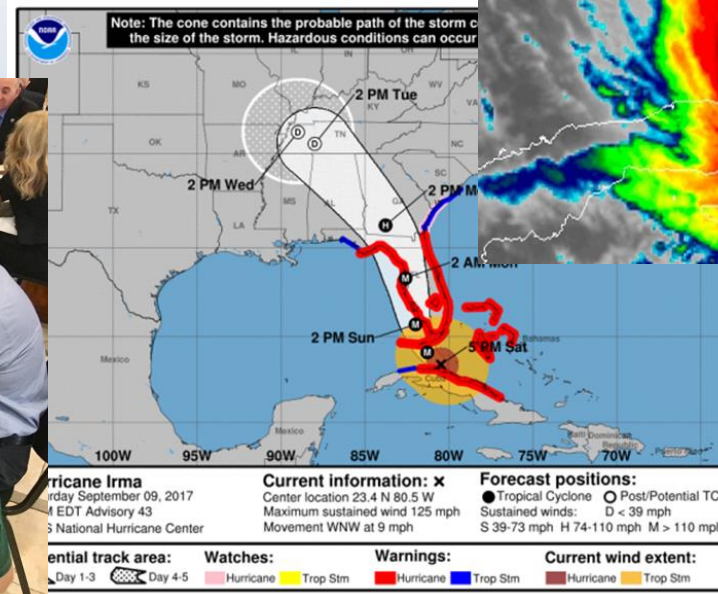

# After Action Review Process



- **Nov. 17:**
  - Foundations After Action Review kickoff meeting
- **December:**
  - Data collection, stakeholder meetings and analysis
- **January:**
  - Jan. 10: Council of Governments meeting
  - Jan. 19: Convocation of Governments Sarasota County Schools
- **February 9:**
  - Facilitated joint meeting with peer reviewers
- **March 14:**
  - Final AAR submitted to the Board of County Commissioners

# What action is being taken now?

## Areas of Focus

- Hurricane Evacuation Center Planning
- Public Education Programs
- Employee Planning and Preparation
- EOC Processes & Information Sharing
- Emergency Contracts






# What action is being taken now?

## ■ Shelter Planning Team

- Find hardened building in central county

## Evacuation Center Planning for Hurricane Season

<b>Feb. / March</b>	Update/develop plans for hurricane evacuation centers.
<b>April</b>	Prepare training for staff and implement public messaging.
<b>May</b>	Implement staff training.
<b>June</b>	Functional exercise for all shelter teams.

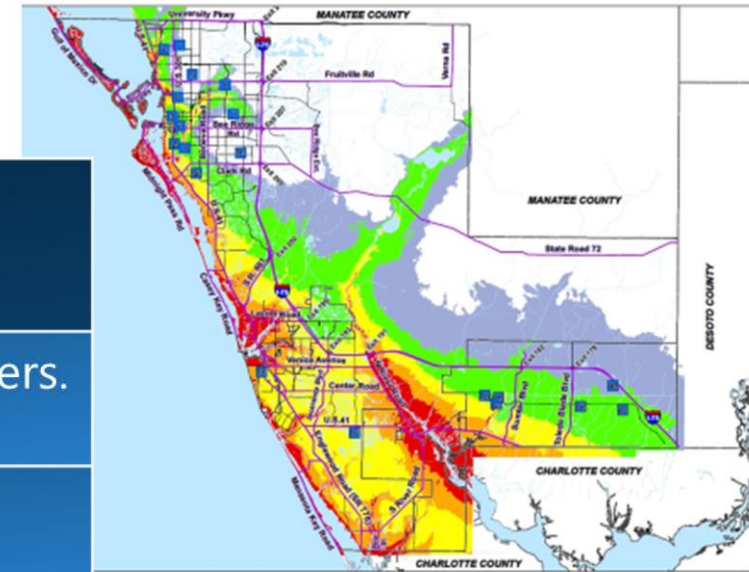

## ■ Coordinated Public Education Messaging Strategy

## What action is being taken now?

- Enhance coordination and collaboration with partners
- Employee messaging, disaster roles and preparedness
- Reviewing and updating communications strategy during EOC activations
- Reviewing power restoration issues with utilities
- Reenergizing Community Organizations Active in Disaster (COAD) relationships and planning
- Memorializing processes during Hurricane Irma response
- Emergency contracts being reviewed and updated
- Mitigation grant availability
- State requests for funding

# Next Steps

## After Action Report/Improvement Plan

### Corrective Action Program

- Area of Improvement
- Recommendations
- Primary Responsible Organization
- Organization Point of Contact
- Timeline for Completion
- Implementation and Tracking



### Mid → Long-Term

- Updated structural analysis for all schools
- Complete plans for upgrading construction of a Venice-area school to EHPA standards
- Identify and prepare any other appropriate EHPA building to a hurricane evacuation center
- Fund construction for upgrade of Venice-area school
- Complete construction of EHPA school in the SR 681 area to be used as a hurricane evacuation center
- Identify funding for adding generators to EHPA shelters



# Questions

